

Providence Hill Road over Providence Hill Brook Construction Report


July 22nd, 2013

Work Completed from July 8th through July 19th:

- Busby Construction placed a water diversion structure around the area of the new culvert and installed sump pumps to keep the work area dry.
- All precast concrete Rigid Frame Box and wing wall fabrication at concrete plant was completed.
- The removal of the old existing corrugated metal pipe culvert was completed and excavation took place in order to prepare the area for the new culvert foundations.
- Storm sewer improvements began by installing storm pipe and manholes on the east side of the project.



Deteriorated corrugated metal pipe culvert being removed from the site.

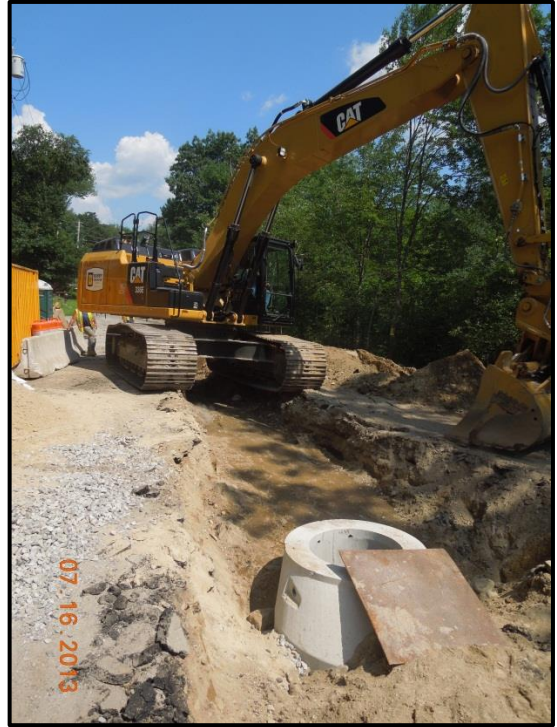

Contractor installing new storm pipe and manhole.



The outlet of the water diversion pipe.



Excavation work continuing to dig down to the proper elevation for the new foundations.

Work Scheduled for July 22th through August 2nd:

- Complete excavations for Rigid Frame Box and wingwall footings.
- Begin construction on the footings for the new Rigid Frame Box.
