


**Cluff Crossing Road / South Policy Street Reconstruction Project**  
**Bi-Weekly Progress Report**  
**May 27, 2011**

This report identifies the work on the Cluff Crossing Road / S. Policy Street project that American Excavating Corporation has completed in the last two (2) weeks and is anticipated to be working on during the next two (2) weeks.

**Last Two (2) Weeks**

- Completed installation of storm drain system between the recently constructed bridge and the Rockingham Mall end of the project.
- Completed installation of storm drain system near the recently constructed bridge and proceeded toward the Kelly Rd. / So. Policy St. / Cross St. intersection.
- Began reclamation operations between the recently constructed bridge and the Rockingham Mall end of the project.

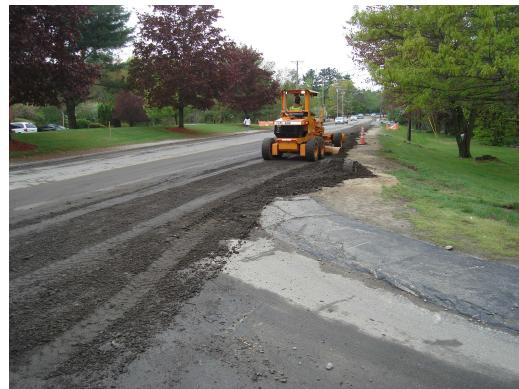

**5/13/11 – Drainage Installation on Cluff Crossing Road near Shaw's Driveway**

**5/16/11 – Pavement Reclamation on Cluff Crossing Road near Shaw's Driveway**

**Next Two (2) Weeks**

- Begin installation of storm drain system on Cross St.
- Complete roadway reclamation of Cluff Crossing Road between the Rockingham Mall driveway and the recently constructed bridge.
- Paving of Base Course and Binder Course on Cluff Crossing Road between the Rockingham Mall driveway and the recently constructed bridge
