

Route 97 / Route 28 (Salem Depot) Intersection Improvements Project
Bi-Weekly Progress Report
March 29, 2021

This report identifies the work on the Salem Depot Intersection project that Linskey Excavating, Co. has completed in the last two (2) weeks and is anticipated to be working on during the next two (2) weeks. Roads will remain open, expect delays. Officers will help you pass through the work zones. Thank you for your patience during the construction process.

Work Completed on Salem Depot Intersection


- Drainage system work continued along the west side of Route 28 to the south of the Salem Depot intersection and began along the southern side of the west leg of Route 97.
- A sewer service was extended to provide future service to 22 S. Broadway
- The hydrant on Route 97 west of the intersection and east of the rail train was relocated to accommodate the new sidewalk.



Extension of an existing sewer service.



Installing a catch basin within a structure box for safety.

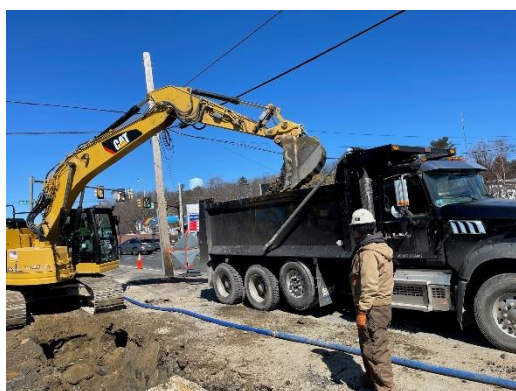

Loading contaminated soil into a dump truck to stockpile prior to disposal.



Relocation of an existing hydrant.

Next Two (2) Weeks

- Drain pipe and catch basin installation will continue along the west side of Route 28 and in the Route 28 / Route 97 Intersection.
- A short segment of water main in front of Dunkin Donuts will be lowered to allow for a larger drain pipe crossing.
- Drain pipe and catch basin installation will be completed in the area adjacent to the former Daisy Cleaner's property.
