BUSBY CONSTRUCTION CO., INC.

71 ROUTE 111
ATKINSON, NH 03811
(603) 898-4800
FAX (603) 898-4808

ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names
1						
2	**Preconstruction Meeting**	1 day	Thu 4/6/17	Thu 4/6/17		
3	**Submit SWPPP/Invasive Species Plan**	1 day	Mon 4/10/17	Mon 4/10/17		
4	**File NOI**	14 days	Mon 4/10/17	Thu 4/27/17		
5	**Receive CAD/Build GPS Model**	10 days	Mon 4/10/17	Fri 4/21/17		
6	**Submittals**	15 days	Mon 4/10/17	Fri 4/28/17		
7	**Set-up Message Boards**	10 days	Mon 4/17/17	Fri 4/28/17		
8	**Secure Dig Safe**	3 days	Mon 4/17/17	Wed 4/19/17		
9	**Establish Initial Survey/Layout**	5 days	Mon 4/24/17	Fri 4/28/17	8	
10	**Erect Traffic Management Signs**	2 days	Thu 4/27/17	Fri 4/28/17		
11	**Preconstruction Video**	1 day	Fri 4/28/17	Fri 4/28/17		
12	**Erosion Control**	2 days	Mon 5/1/17	Tue 5/2/17	9	
13	**Tree Trimming, Clear, Remove Trees & Grub**	4 days	Mon 5/1/17	Thu 5/4/17		
14	Exploratory Excavation	2 days	Wed 5/3/17	Thu 5/4/17		
15	**Remove Stumps**	2 days	Thu 5/4/17	Fri 5/5/17		
16	**Drainage Improvements-Haverhill Rd**	19 days	Mon 5/8/17	Thu 6/1/17	15	
17	**Rock Structure Excavation**	19 days	Mon 5/8/17	Thu 6/1/17		
18	**Drainage Improvements-Klein Dr**	5 days	Fri 6/2/17	Thu 6/8/17		
19	**Common Excavation-Haverhill Rd**	25 days	Mon 6/5/17	Fri 7/7/17		
20	**Rock Excavation-Haverhill Rd**	25 days	Mon 6/5/17	Fri 7/7/17		
21	Crushed Stone Coarse-Haverhill Rd	28 days	Mon 6/5/17	Wed 7/12/17		
22	Dry Hydrant Removal	1 day?	Fri 6/9/17	Fri 6/9/17		
23	**Cofferdam, Drain Pipe, Headwalls**	5 days	Fri 6/9/17	Thu 6/15/17		
24	Excavate & Pour Mast Arm Foundation	5 days	Mon 6/19/17	Fri 6/23/17	23	
25	**Crushed Stone Fine-Haverhill Rd**	4 days	Thu 7/13/17	Tue 7/18/17	24	
26	**Fine Grade-Haverhill Rd**	2 days	Wed 7/19/17	Thu 7/20/17	25	
27	**Pave Binder-Haverhill Rd**	1 day	Fri 7/21/17	Fri 7/21/17		
28	**Reclaimed Stablized Base, In Place-Klein DR**	1 day	Mon 7/24/17	Mon 7/24/17		
29	**Reclaimed Stabilized Base, R & R,-Klein DR**	2 days	Tue 7/25/17	Wed 7/26/17		
30	**Prep & Pave Driveways Binder-Haverhill Rd**	5 days	Mon 7/24/17	Fri 7/28/17		
31	**Common Excavation-Klein Dr**	1 day	Wed 7/26/17	Wed 7/26/17		
32	**Crushed Stone Coarse-Klein Dr**	2 days	Thu 7/27/17	Fri 7/28/17		
33	Install Mast Arm/Signalization	5 days	Mon 7/31/17	Fri 8/4/17		
34	**Place R & R Reclaimed Asphalt**	2 days	Mon 7/31/17	Tue 8/1/17		
35	**Fine Grade-Klein Dr**	1 day	Wed 8/2/17	Wed 8/2/17	34	
36	Pave Binder-Klein Dr	1 day?	Thu 8/3/17	Thu 8/3/17		
37	Shape Swales & Shoulder-Haverhill & Klein	10 days	Fri 8/4/17	Thu 8/17/17		
38	Stone Wall Reconstruction	10 days	Fri 8/4/17	Thu 8/17/17		
39	Prep & Pave Driveways Binder-Klein Dr	5 days	Fri 8/4/17	Thu 8/10/17		
40	Curbing-Granite & Bituminous	2 days	Mon 8/14/17	Tue 8/15/17		
41	Turf Establishment	5 days	Fri 8/18/17	Thu 8/24/17		
42	Construct Platforms/Install Guardrail	2 days	Fri 8/25/17	Mon 8/28/17		
43	R & R Mailboxes	2 days	Tue 8/29/17	Wed 8/30/17		
44	R & R Landscaping/Trees	4 days	Thu 8/31/17	Tue 9/5/17		
45	Raise Structures	2 days	Wed 9/6/17	Thu 9/7/17		
46	Cold Plane	1 day?	Thu 9/7/17	Thu 9/7/17		
47	Pave Wearing Surface	1 day?	Fri 9/8/17	Fri 9/8/17		
48	Pave Wearing Surface Driveways	2 days	Mon 9/11/17	Tue 9/12/17		
49	Install Signs/Delineators	1 day?	Tue 9/12/17	Tue 9/12/17		
50	Crushed Aggregate Shoulders	1 day?	Wed 9/13/17	Wed 9/13/17		
51	Clean up/Punch List	4 days	Thu 9/14/17	Tue 9/19/17		
52	Pavement Markings	1 day?	Fri 9/15/17	Fri 9/15/17		
53	Reset Monuments	1 day?	Mon 9/18/17	Mon 9/18/17		
54	Remove Traffic Management Signs	1 day?	Tue 9/19/17	Tue 9/19/17		
55	Close-out Documents	15 days	Tue 9/19/17	Mon 10/9/17		

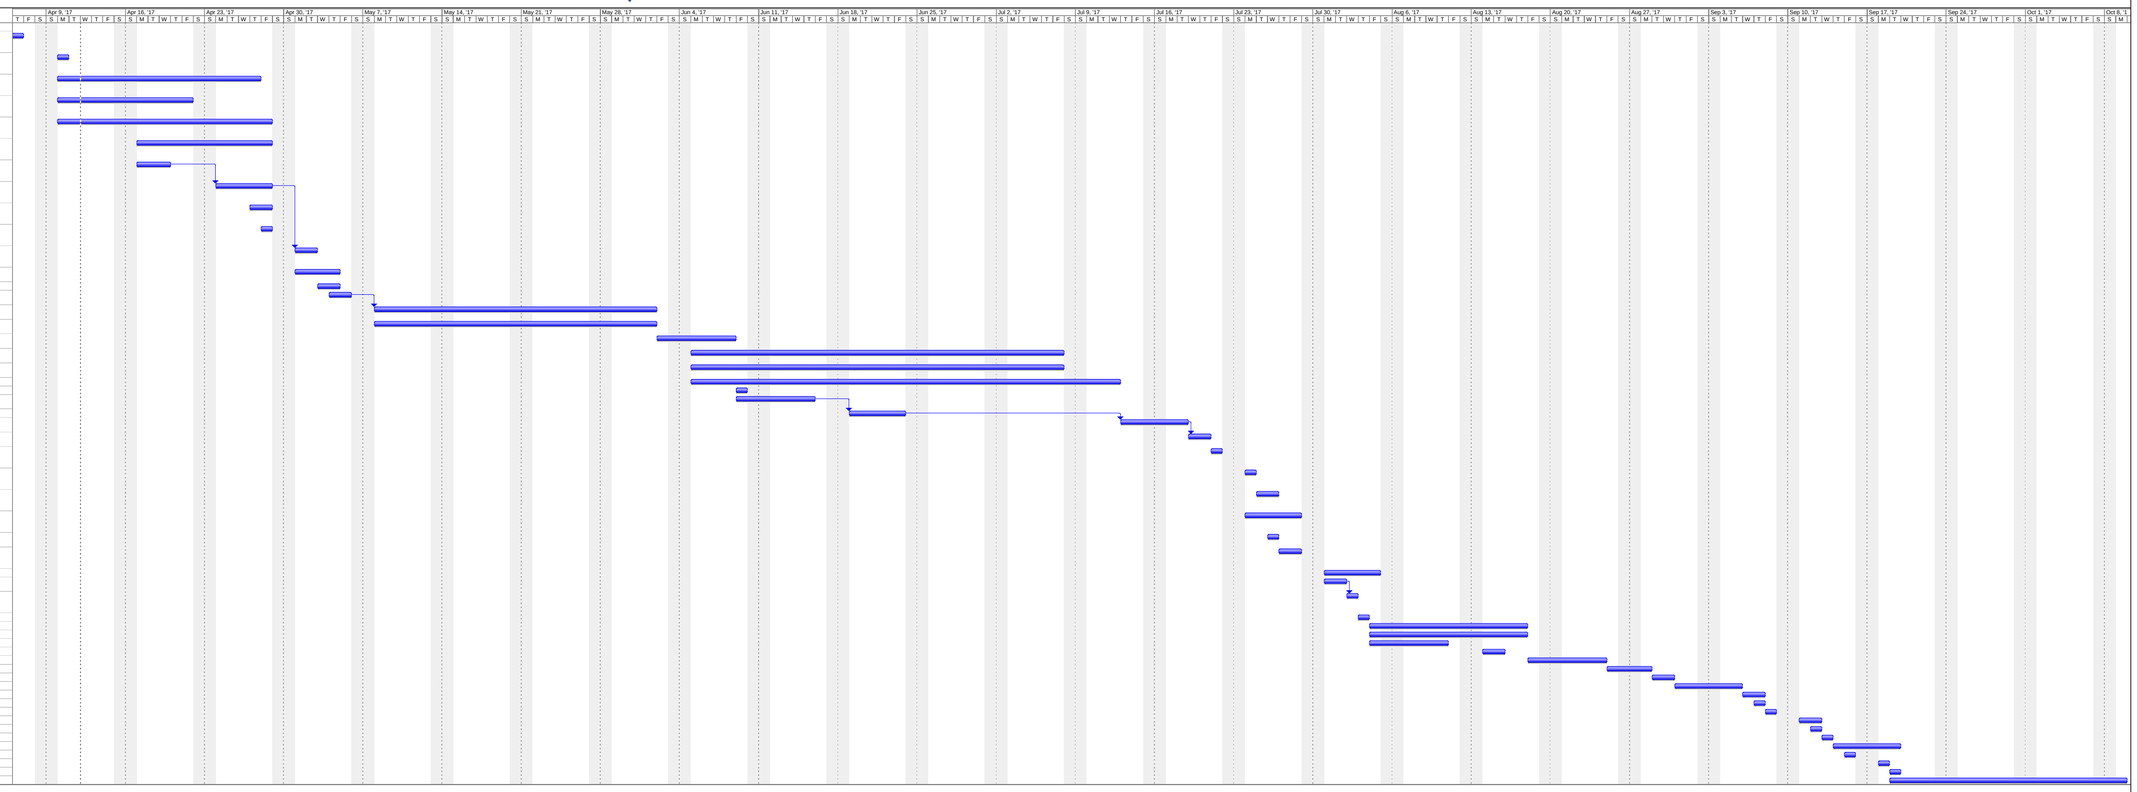

Project: Haverhill Rd & Klein Dr
Date: Wed 4/12/17

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline
